

Water System Improvements Project Status Update

Martin County Water District


November 18, 2020

Status Report (BSADD/Bell)

► Funding

- AML Pilot NEXUS Grant (2017) - \$3,450,000
- COE 531 Partnership - \$1,869,718
- ARC Grant - \$1,200,000
- AML Pilot NEXUS Grant (2018) - \$2,000,000
- KYTC Bridging Kentucky Funds - Willis Dials / Dan's Branch Road - \$38,357
- Hunters Lane & Rockhouse Creek - To Be Determined

► Total Grant Funding - \$8,558,075

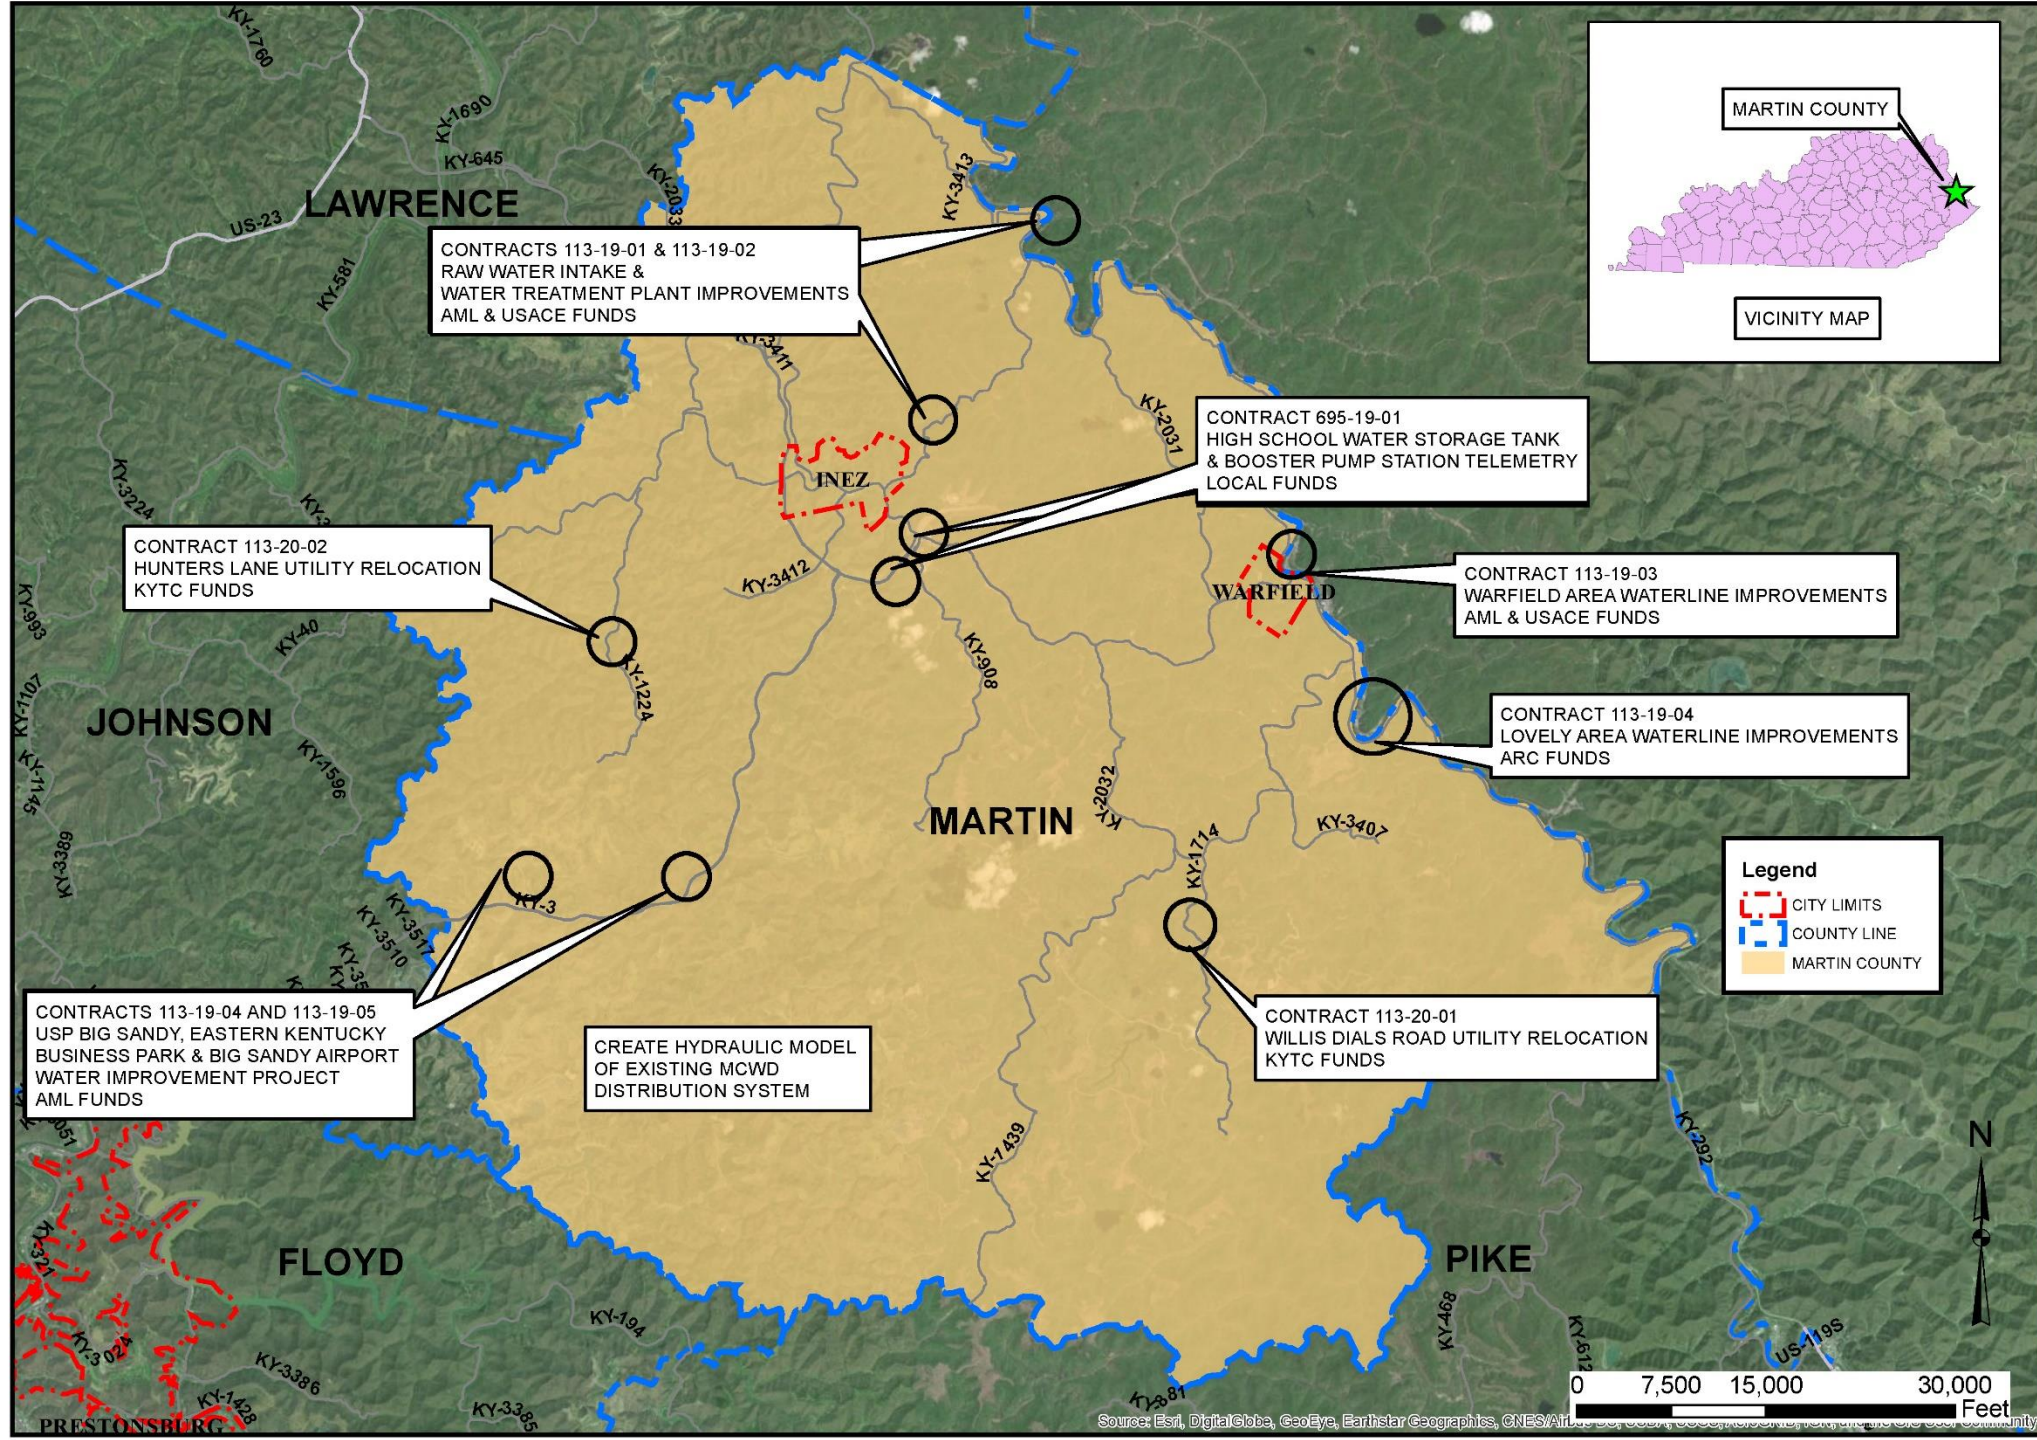

ALL RIGHTS RESERVED
THIS DOCUMENT IS THE PROPERTY OF BELL
ENGINEERING. IT SHALL NOT BE REPRODUCED,
IN WHOLE OR IN PART OR USED FOR CONSTRUCTION
OF OTHER THAN THIS SPECIFIC PROJECT WITHOUT
THE WRITTEN PERMISSION OF BELL ENGINEERING



Contract 113-19-01

RWI Improvements Pump Purchase Only

► Purchase of:

- New 2 MG Raw Water Intake Pump with Variable Speed Drive
- New 4 MG Raw Water Intake Pump with Variable Speed Drive
- New 4,000 GPM River Screen

► Budget: \$601,200

► Funding: Abandoned Mine Lands 2017 NEXUS

► Status:

- Design, Bidding & Fabrication - Complete
- MCWD currently utilizing 2 MGD Pump.
- 4 MGD Pump to be placed in service upon completion of Contract 113-19-02.



Contract 113-19-02

RWI & WTP Improvements

► Raw Water Intake Improvements:

- Concrete Ramp & Winch System for Moving Raw Water Pumps Up & Down Slope
- Electrical Building Upgrade, Telemetry, Line Reactors and Instrumentation

► Water Treatment Plant Improvements:

- Clarifiers 1 & 3 Rehabilitation with New Valve Vault for Clarifier 1
- Replace Outside Chlorine Chemical Feed Piping & Roof On Chemical Storage Building
- Replace Master Meter
- 500 KVA on-site Backup Generator

► Budget: \$3,098,860

► Funding: Abandoned Mine Lands 2017 NEXUS & Army Corps of Engineers

Contract 113-19-02 (Continued)

RWI & WTP Improvements

► Status:

- Permits are in place.
- Authorization To Proceed with Bidding Granted.
- Project is currently out for bids.
- Schedule:

Pre-Bid Meeting for interested Contractors - December 1, 2020.

Bid Opening - December 15, 2020.

Anticipated Contract Award - Late December 2020.

Anticipated Start of Construction - Early February 2021 (300-day contract).

Anticipated End of Construction - Early December 2021



Contract 113-19-03

Mainline, Service Line, Meter Replacement

- ▶ **Replace in the Warfield Area:**
 - Existing Mainline
 - Existing Meters & Service Line
 - Existing Valves & Hydrants
- ▶ **Total Project Budget:** \$1,260,658
- ▶ **Funding:** Abandoned Mine Lands 2017 NEXUS & Army Corps of Engineers



Contract 113-19-03 (Continued)

Mainline, Service Line, Meter Replacement

► Status

- Permits are in place.
- Authorization To Proceed with Bidding Granted.
- Project is currently out for bids.
- Schedule:

Pre-Bid Meeting for interested Contractors - December 1, 2020.

Bid Opening - December 15, 2020.

Anticipated Contract Award - Late December 2020.

Anticipated Start of Construction - Early February 2021 (130-day contract).

Anticipated End of Construction - Mid June 2021

Contract 113-19-04

Mainline, Service Line, Meter Replacement

- ▶ **Upgrades in the Lovely Area include the Replacement of:**
 - Existing Mainline, Meters, Service Line, Valves & Hydrants
- ▶ **Budget:** \$1,200,000
- ▶ **Funding:** Appalachian Regional Commission (ARC)
- ▶ **Status:**
 - Project is under Construction.
 - Anticipated Completion Date: March 20, 2021



Contracts 113-19-05 & 113-19-06

USP Big Sandy, Eastern Kentucky Business Park & Big Sandy Airport Water Improvements

► Upgrades Include:

- Construction of 250,000 Gallon Water Storage Tank, New 400 GPM Pump Station and telemetry
- Upgrade of the Existing Davella Pump Station
- Master Meter & Booster Chlorination

► Budget: \$2,000,000

► Funding: Abandoned Mine Lands 2018 NEXUS

► Status:

- The previously selected tank site cannot be used.
- Currently evaluating three potential new sites.



Contract 695-19-01

High School Water Storage Tank & Booster Pump Station Telemetry

► Upgrades Include:

- Add telemetry to the Holly Bush Pump Station
- Add telemetry to the High School Water Storage Tank

► Budget: \$65,000

► Funding: Local Funds (Martin County Fiscal Court)

► Status:

- Design: Complete
- Bidding: Complete
- Award: Complete
- Materials Fabrication: Complete
- Construction: All equipment installed.



Contract 113-20-01

Willis Dials/Dan's Branch Road Utility Relocation

► Upgrades Include:

- Relocation of existing waterline to facilitate construction of a new bridge for the KYTC Bridging Kentucky Program

► Budget: \$38,357

► Funding: KYTC

► Status:

- Project approved by Division of Water August 13, 2020.
- Construction completed September 24, 2020.



Contracts 113-20-02 and 113-20-03

Hunters Ln. & Rockhouse Creek Utility Relocations

► Upgrades Include:

- Relocation of existing waterline to facilitate construction of two new bridges for the KYTC Bridging Kentucky Program

► Budget: To Be Determined

► Funding: KYTC


► Status:

- Developing project scope with Bizzack Construction and Alliance Resources. Construction scheduled for Summer 2021.



Martin County Water District Hydraulic Model

- ▶ Prepare and Calibrate a Hydraulic Model of the Martin County Water District System
- ▶ Budget: \$100,000
- ▶ Funding: Abandoned Mine Lands 2017 NEXUS
- ▶ Status:
 - Lines, tanks and PRVs have been input into the model and location field verified.
 - Line sizes have been verified.
 - Pressure zones have been analyzed.
 - Usage data has been entered into the model.
 - Model has been calibrated with field collected data.
 - Model has been checked against field observations.

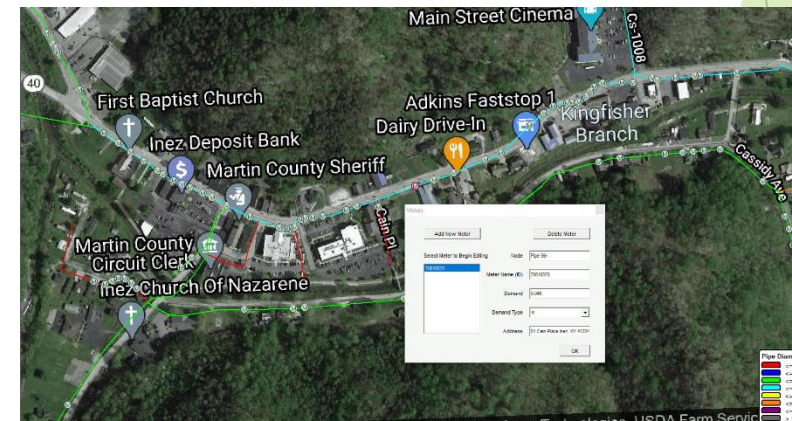

Discussion/Questions
